

Work Order ID - 152087

152087

Page 1

Wednesday, October 19, 2016 3:28:41 PM

Item ID: PB67-43001-239W

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: Square Tube Weldment

Start Date: 10/13/2016 Start Qty: 1.00

1

Cust Item ID:

Required Date: 10/19/2016 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: **DAS**
21
9-89

Date: OCT 20 2016

Tooling:

Date:

Run Start

NR1

QC:

Date:

SPC (Y/N):

Date:

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
--------------------------------	--------------------------	----------------------	---------	--------	--------------	---------------	---------------	------------------	----------------

Draw Nbr	Revision Nbr
----------	--------------

B67-43001-239	D
---------------	---

110

Weld per dwg A/R Aluminum rod Batch:

0.00

110

Large Fab

Memo

0.00

Large Fab

- 1- Cut to length as per dwg
- 2- Make a chamfer on both ends of tube
- 3- Drill holes as per dwg use drill jig DT10022
- 4- Make a chamfer on both side of the 4 holes
- 7- Deburr

120

QC10- Inspect visual per QSI004- ground welds

0.00

120

QC

Memo

0.00

Quality Control

16.11.28

1 FF NOV 25 2016

DAS
9
9-89
16.12.07

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	

Root Cause			FAULT CATEGORY					
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐			
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐			
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐			
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐			
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐			
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐			
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐			
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐			
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐			
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐			
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :						
Misidentified ☐	Past Due ☐							

Wednesday, October 19, 2016 3:28:41 PM

Page 2

Quality Control

DA
9
9-8.8

16.12.07

MF 16-12-15

16/12/15

MF
16-12-15

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
				Completed By					
				Lead hand / Supervisor Approval Verification					
				QC / QA Coordinator Approval					

Root Cause				FAULT CATEGORY							
Environment	☐	No Re-verification	☐	Pressure/Forced	☐	Temperature/Cure	☐	Power Loss/Surge	☐	Positioned Wrong	☐
Design	☐	Operator	☐	Bending	☐	Set-up	☐	Folio/Program	☐	Outside Dimensions	☐
Doc/Data	☐	Offset/Setup	☐	Centre Not Concentric	☐	BOM/Route	☐	Grain	☐	Over/Under tolerance	☐
Equip/Tooling	☐	Supplier	☐	Cracks	☐	Broken/Damage/Defect	☐	Weld	☐	Part Incorrect	☐
Handling/Pre	☐	Training	☐	Crimp/Kink/Ripple/Wave	☐	Inspection Incomplete/Unqualified	☐	Wrong Stock Pulled	☐	Part Lost/Missing	☐
Material	☐	Use for Testing	☐	Cuffs	☐	Contamination	☐	Out of Sequence	☐	Part Moved	☐
Internal Transport	☐	Poor Information	☐	Crushing	☐	Countersink	☐	Off-set	☐	Drawing	☐
Tribal Knowledge	☐	Rushing	☐	Heat Treat	☐	Cut Too Short	☐	Mislabeled	☐	Finish	☐
LOA	☐	Product Improvement	☐	Wave/Twist in Tube	☐	Instructions Incomplete/Unclear	☐	Fit/Function	☐	Misread	☐
Substation	☐	Process Improvement	☐	Marks/Chatter	☐	Drill Holes	☐	Misaligned/off center	☐	Turning Sequence	☐
Past Expiry Date	☐	Manufacturing Process	☐	OTHER :							
Misidentified	☐	Past Due	☐								

Picklist Print

Wednesday, October 19, 2016 3:28:41 PM

Page 1

Work Order ID: 152087

152087

Parent Item: PB67-43001-239W

PR67-43001-239W

Parent Item Name: Square Tube Weldment

Start Date: 10/13/2016

Required Date: 10/19/2016

Start Qty: 1.00

Required Qty: 1.00

Comments: IPP REV:A 15.04.02 NEW ISSUE DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M6061T6TS1.000W.125		Purchased	No				f	21.5000		1.842105			

M6061T6TS1 000W 125

6061T6 SQ TUBE 1.00 x 1.00 x .125w

**

NOV 25 2016

Location

Loc Qty

Loc Code

MAT028

21.499953

m128034

21.499953

PB67-43001-223

Manufactured No

Each

1.0000

1

PR67-43001-223

Square Cap

**

Location

Loc Qty

Loc Code

Mezz2

1

133770

1

PB67-43001-225

Manufactured No

Each

27.0000

4

PR67-43001-225

Bushing

**

Location

Loc Qty

Loc Code

Mezz2

27

148791

27

1.842105

ME 16-11-24

ME 16-11-24

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐		No Re-verification ☐		Pressure/Forced ☐		Temperature/Cure ☐	
Design ☐		Operator ☐		Bending ☐		Set-up ☐	
Doc/Data ☐		Offset/Setup ☐		Centre Not Concentric ☐		BOM/Route ☐	
Equip/Tooling ☐		Supplier ☐		Cracks ☐		Broken/Damage/Defect ☐	
Handling/Pre ☐		Training ☐		Crimp/Kink/Ripple/Wave ☐		Inspection Incomplete/Unqualified ☐	
Material ☐		Use for Testing ☐		Cuffs ☐		Contamination ☐	
Internal Transport ☐		Poor Information ☐		Crushing ☐		Countersink ☐	
Tribal Knowledge ☐		Rushing ☐		Heat Treat ☐		Cut Too Short ☐	
LOA ☐		Product Improvement ☐		Wave/Twist in Tube ☐		Instructions Incomplete/Unclear ☐	
Substation ☐		Process Improvement ☐		Marks/Chatter ☐		Drill Holes ☐	
Past Expiry Date ☐		Manufacturing Process ☐		OTHER :			
Misidentified ☐		Past Due ☐					

ITEM	QTY -239W	P/N	DESCRIPTION
	X	B67-43001-239W	SQUARE TUBE WELDMENT
1	1	B67-43001-223	SQUARE CAP
2	4	B67-43001-225	BUSHING
3	1	B67-43001-239	



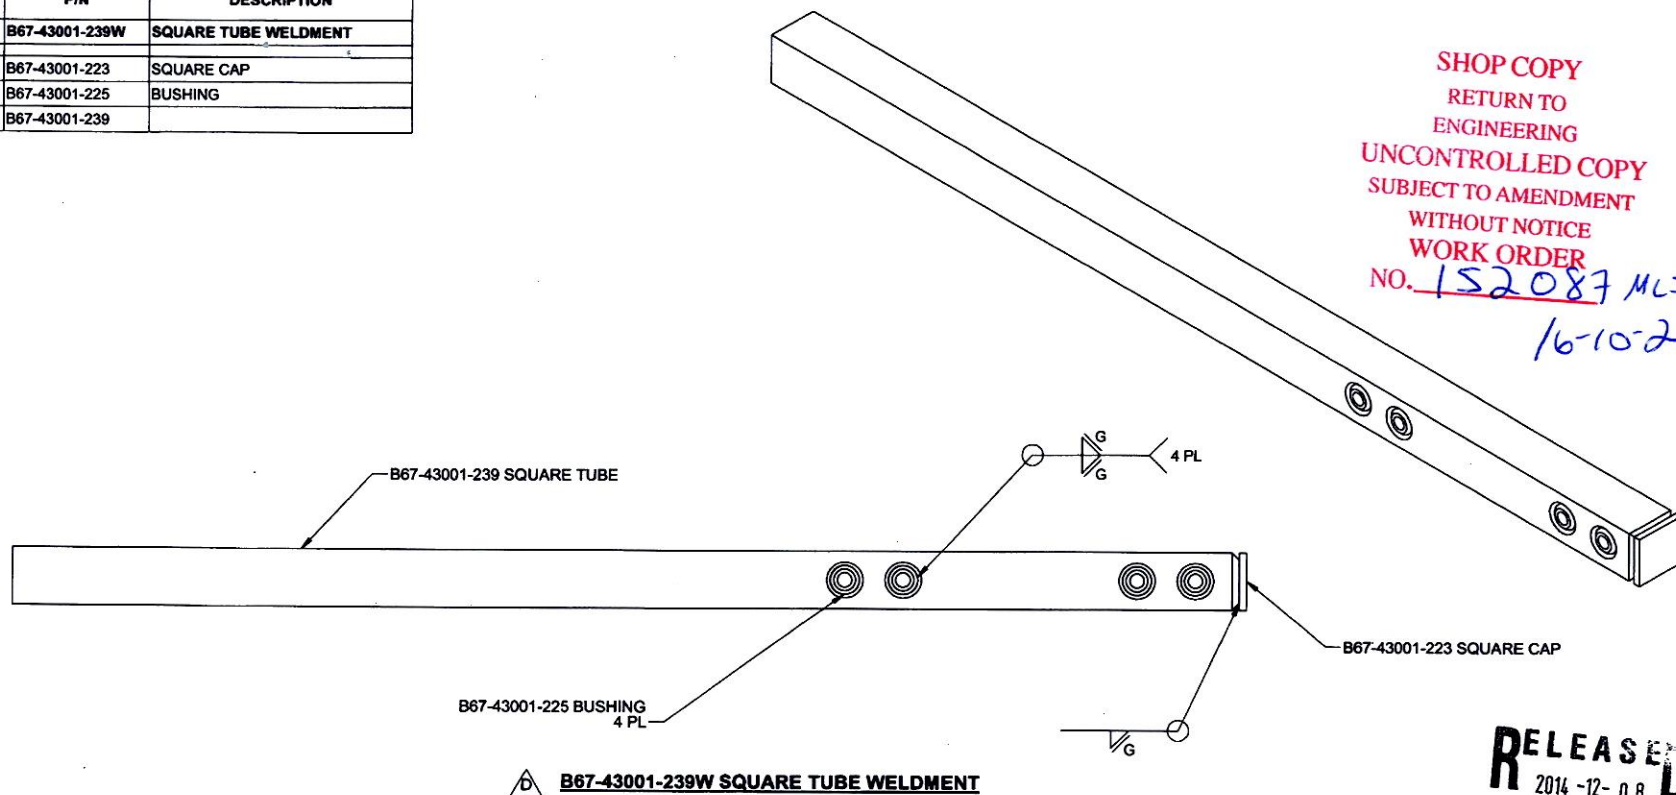


SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 152087 ML5
16-10-20

RELEASE
2014-12-08
MP

- NOTES:
- 1) MATERIAL: N/A
 - 2) FINISH: N/A
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: N/A
 - 7) WEIGHT: 0.94 lbs
 - 8) WELDING: PER DART QSI 004

D	ADD -239W WELDMENT. REMOVE CHAMFER (ZIN C4-2). REASON: TO FACILITATE MANUFACTURING	DB	14.07.22
C	REDRAWN PREMIER AVIATION DRAWING IAW DART QSI 018 AND QSI 043. FOR PREVIOUS REVISIONS, REFER TO PAGE 21 OF PREMIER AVIATION DRAWING No. B67-43001. REASON: SEE PAR009-011.	MB	09.02.19
REV.	DESCRIPTION	BY	DATE
DESIGN	RW	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	DB		
CHECKED		DRAWING NO.	REV. D
MFG. APPR.	<i>[Signature]</i>	B67-43001-239	SHEET 1 OF 2
APPROVED	<i>[Signature]</i>	TITLE	SCALE
DE APPR.	N/A	SQUARE TUBE	NTS
DATE	14.07.22	COPYRIGHT © 1985 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

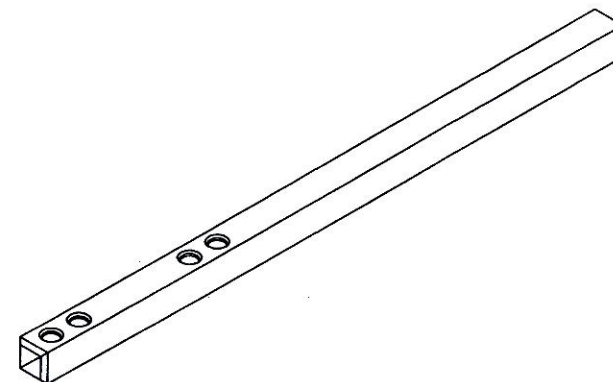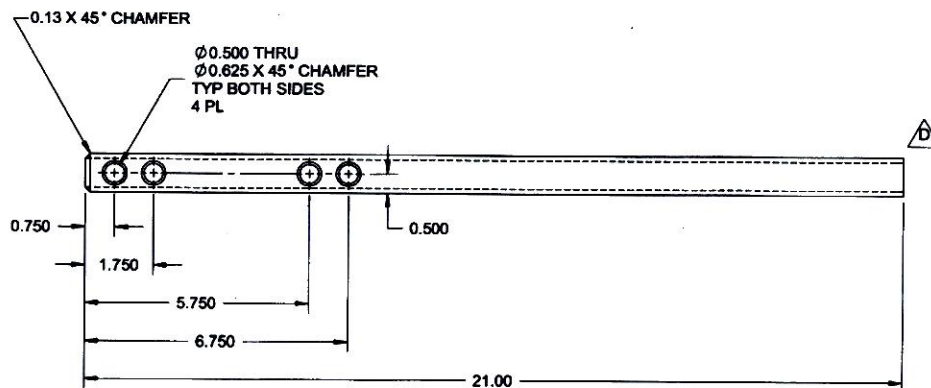

B67-43001-239 SQUARE TUBE

RELEASE
2014-12-08

NOTES:

- 1) MATERIAL: 6061-T6 (OR 6061-T651/T6510/T6511/T62) SQUARE TUBING
PER AMS-QQ-A-225/8 (OR AMS 4117/4128/4115/4116) OR
PER AMS-QQ-A-200/8 (OR AMS 4160)
REF. DART SPEC. M6061T6TS1.000W0.125
- 2) FINISH: N/A
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: N/A
- 7) WEIGHT: 0.87 lbs

DESIGN	RW	DART AEROSPACE LTD	
DRAWN	DB	HAWKESBURY, ONTARIO, CANADA	
CHECKED	5	DRAWING NO.	REV. D
MFG. APPR.		B67-43001-239	SHEET 2 OF 2
APPROVED		TITLE	SCALE
DE APPR.	N/A	SQUARE TUBE	NTS
DATE	14.07.22	COPYRIGHT © 1995 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL, AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	
